ID	Task Name	Duration	Start	Finish
1	**MOSH NOISE TEAM STRAT. PLAN - 2014**	**266 days?**	**Thu 1/16/14**	**Thu 1/22/15**
2	Year Start	0 days	Thu 1/16/14	Thu 1/16/14
3	**Strategic Objective 1 - Facilitate the HPD TAS Adoption**	**189 days**	**Thu 1/16/14**	**Wed 10/8/14**
4	**Goal 1 - Establish effective COPAs by June 2014**	**189 days**	**Thu 1/16/14**	**Wed 10/8/14**
5	Request nominations from Mine Adoption Managers	2 wks	Thu 1/16/14	Wed 1/29/14
6	Approval of COPA Nominees by MOSH Task Force	2 wks	Thu 1/30/14	Wed 2/12/14
7	Draft Portfolio of Evidence (PoE) for HPD TAS adoption	44 days	Thu 1/16/14	Tue 3/18/14
8	First COPA Meeting	0 days	Wed 3/26/14	Wed 3/26/14
9	Second COPA Meeting	0 days	Wed 5/7/14	Wed 5/7/14
10	Third COPA Meeting	0 days	Wed 7/9/14	Wed 7/9/14
11	Fourth COPA Meeting	0 days	Wed 10/8/14	Wed 10/8/14
12	**Milestone 1 - HPD TAS COPAs established**	0 days	Wed 10/8/14	Wed 10/8/14
13	**Strategic Objective 2 - Identify a new Leading Practice**	**233 days**	**Thu 1/16/14**	**Mon 12/8/14**
14	**Goal 2 - Planning workshop by June 2014**	**89 days**	**Thu 1/16/14**	**Wed 5/21/14**
15	Continue to Solicit Leading Practices from Mining Houses	2 mons	Thu 1/16/14	Wed 3/12/14
16	Compiling and analyzing Noise Statistics	1 mon	Thu 1/16/14	Wed 2/12/14
17	Review the Noise Risk Summary (including workshop prep work)	2.5 mons	Thu 2/13/14	Wed 4/23/14
18	**Milestone 2 - Successful Planning workshop**	0 days	Wed 5/21/14	Wed 5/21/14
19	**Goal 3 - Document the Identified Leading Practice**	**64 days**	**Wed 5/21/14**	**Tue 8/19/14**
20	Document the Leading Practice	3 mons	Wed 5/21/14	Tue 8/12/14
21	**Milestone 3 - Successful leading practice documentation**	0 days	Tue 8/19/14	Tue 8/19/14
22	**Goal 4 - Demonstrate/ Facilitate the Leading Practice**	**80 days**	**Tue 8/19/14**	**Mon 12/8/14**
23	Demonstrate/ Facilitate the Leading Practice	4 mons	Tue 8/19/14	Mon 12/8/14
24	**Milestone 4 - Facilitation of the Identified Leading Practice**	0 days	Mon 12/8/14	Mon 12/8/14
25	**Strategic Objective 3 - Facilitate the IBMQI**	**266 days?**	**Thu 1/16/14**	**Thu 1/22/15**
26	**Goal 5 - Establish the IBMQI Working Group**	**66 days?**	**Thu 1/16/14**	**Thu 4/17/14**
27	Solicit Approval of the Nominees from the MOSH Task Force Members	26 days?	Thu 1/16/14	Thu 2/20/14
28	Operationalisation of the Working Group (Detailed Scoping, election of Chair etc)	2 mons	Fri 2/21/14	Thu 4/17/14
29	**Milestone - 5 - IBMQI Working Group Established**	0 days	Thu 4/17/14	Thu 4/17/14
30	**Goal 6 - Establish Task Specific Working Group**	**40 days**	**Fri 4/18/14**	**Thu 6/12/14**
31	Establishment of Task Specific Working Groups	2 mons	Fri 4/18/14	Thu 6/12/14
32	**Milestone 6 - Task Specific Working Groups are established**	0 days	Thu 6/12/14	Thu 6/12/14
33	**Goal 7 - Preliminary setting of envisaged noise reduction Targets**	**120 days**	**Fri 6/13/14**	**Thu 11/27/14**
34	Noise Reduction Targets are set	6 mons	Fri 6/13/14	Thu 11/27/14
35	**Milestone 7 - Noise Reduction Targets are set**	0 days	Thu 11/27/14	Thu 11/27/14
36	**Goal 8 - Set up Round table discussions with Supplier executives**	**40 days**	**Fri 11/28/14**	**Thu 1/22/15**
37	Set Round table discussions with Supplier executives	2 mons	Fri 11/28/14	Thu 1/22/15
38	Milestone 8 - Successful Round table discussions with Supplier executives	0 days	Thu 1/22/15	Thu 1/22/15
39	Year End	0 days	Thu 1/22/15	Thu 1/22/15

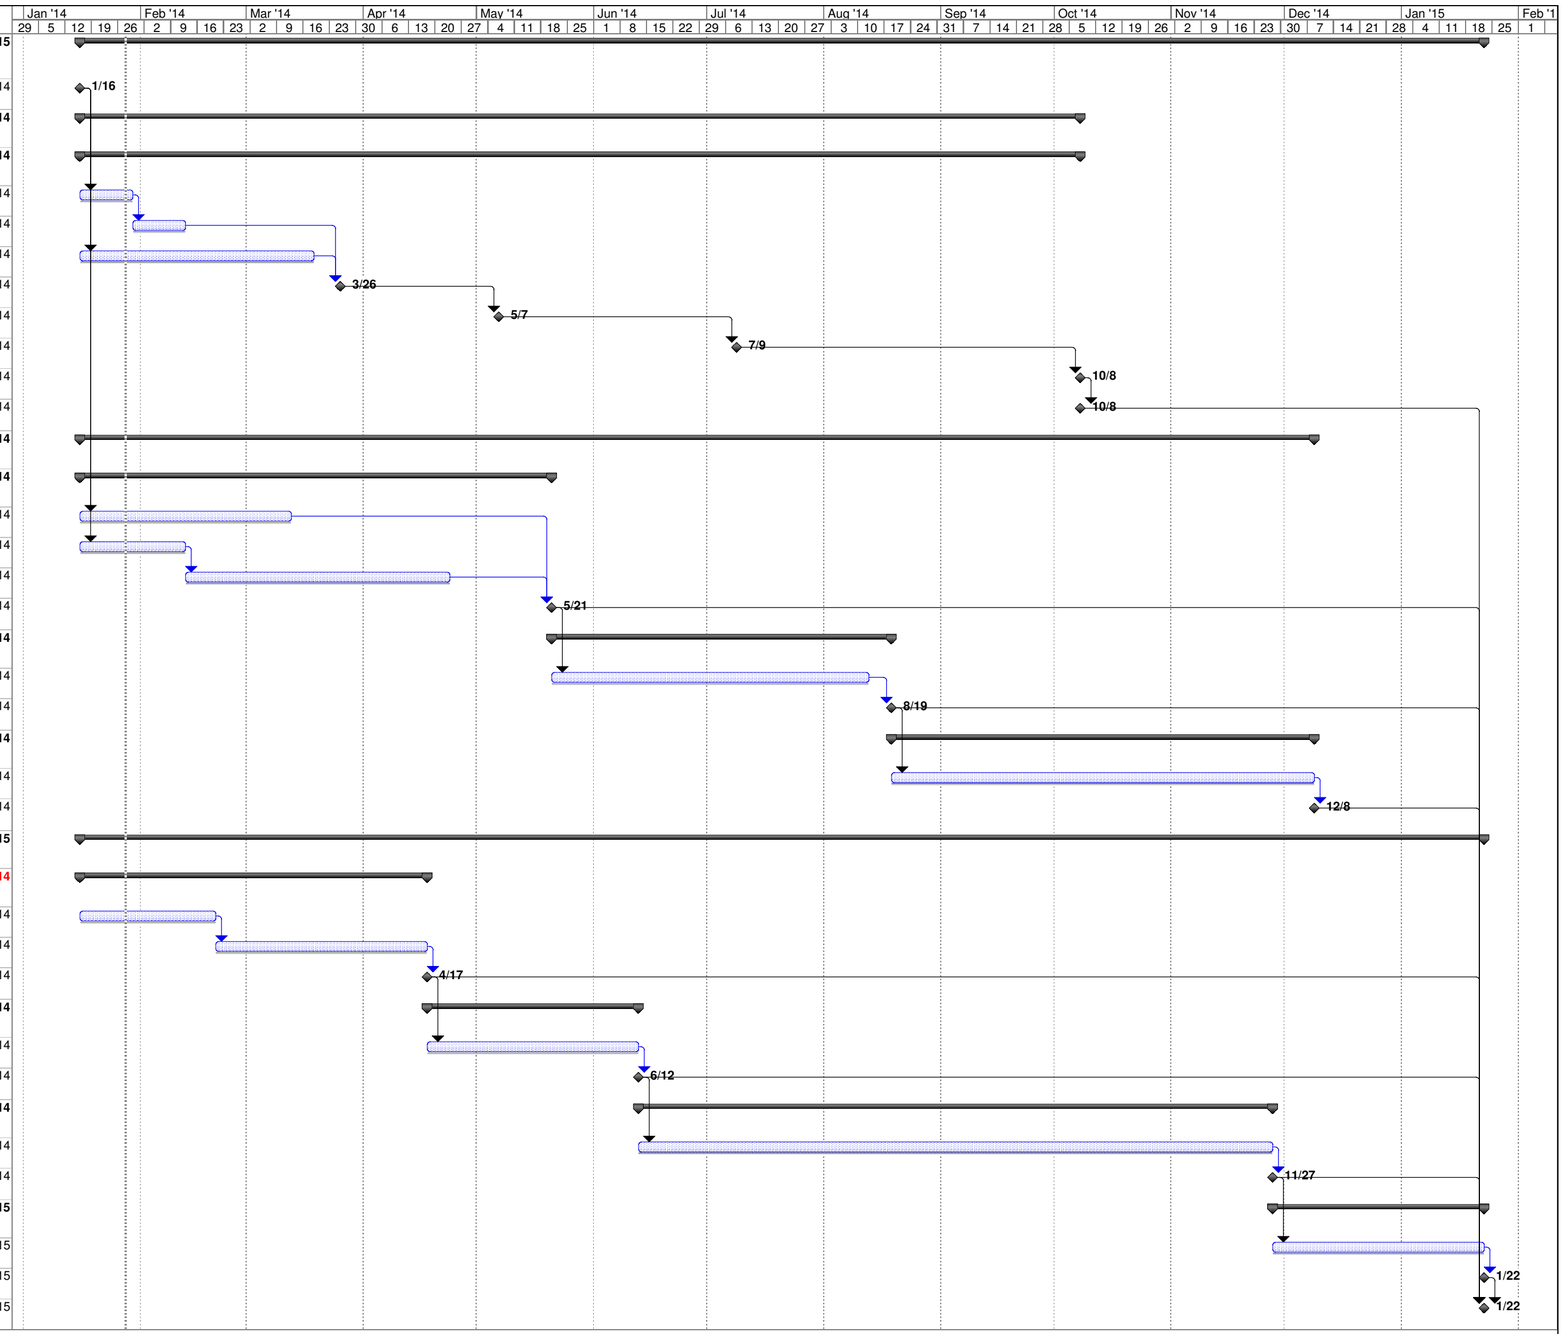

Project: MOSH Team Annual Strat Pla
Date: Tue 1/28/14

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External MileTask | Split
